ID	Task Mode	Task Name	Duration	Start	Finish
1		**Mobilization**	3 days	Mon 11/4/24	Wed 11/6/24
2		**Delivery #1**	1 day	Tue 11/5/24	Tue 11/5/24
3		**13907B**	**19 days**	**Tue 11/5/24**	**Fri 11/29/24**
4		Disconnect HVAC	3 days	Tue 11/5/24	Thu 11/7/24
5		Demolition	4 days	Tue 11/5/24	Fri 11/8/24
6		Roofing	9 days	Tue 11/5/24	Fri 11/15/24
7		Reconnect HVAC	5 days	Mon 11/18/24	Fri 11/22/24
8		Sheet Metal	10 days	Mon 11/18/24	Fri 11/29/24
9		**14007A**	**22 days**	**Wed 11/13/24**	**Thu 12/12/24**
10		Disconnect HVAC	3 days	Wed 11/13/24	Fri 11/15/24
11		Demolition	4 days	Mon 11/18/24	Thu 11/21/24
12		Roofing	9 days	Mon 11/18/24	Thu 11/28/24
13		Reconnect HVAC	5 days	Fri 11/29/24	Thu 12/5/24
14		Sheet Metal	10 days	Fri 11/29/24	Thu 12/12/24
15		**14007B**	**24 days**	**Mon 11/25/24**	**Thu 12/26/24**
16		Disconnect HVAC	3 days	Mon 11/25/24	Wed 11/27/24
17		Demolition	4 days	Mon 12/2/24	Thu 12/5/24
18		Roofing	9 days	Mon 12/2/24	Thu 12/12/24
19		Reconnect HVAC	5 days	Fri 12/13/24	Thu 12/19/24
20		Sheet Metal	10 days	Fri 12/13/24	Thu 12/26/24
21		**14007C**	**23 days**	**Tue 12/10/24**	**Thu 1/9/25**
22		Disconnect HVAC	3 days	Tue 12/10/24	Thu 12/12/24
23		Demolition	4 days	Fri 12/13/24	Wed 12/18/24
24		Roofing	9 days	Fri 12/13/24	Wed 12/25/24
25		Reconnect HVAC	5 days	Thu 12/26/24	Wed 1/1/25
26		Sheet Metal	10 days	Fri 12/27/24	Thu 1/9/25
27		**411**	**21 days**	**Thu 12/26/24**	**Thu 1/23/25**
28		Disconnect HVAC	3 days	Thu 12/26/24	Mon 12/30/24
29		Demolition	4 days	Thu 12/26/24	Tue 12/31/24
30		Roofing	9 days	Thu 12/26/24	Tue 1/7/25
31		Reconnect HVAC	5 days	Wed 1/8/25	Tue 1/14/25
32		Sheet Metal	10 days	Fri 1/10/25	Thu 1/23/25
33		**Delivery #2**	1 day	Mon 1/13/25	Mon 1/13/25
34		**13908C**	**26 days**	**Thu 1/2/25**	**Thu 2/6/25**
35		Disconnect HVAC	3 days	Thu 1/2/25	Mon 1/6/25
36		Demolition	4 days	Wed 1/8/25	Mon 1/13/25
37		Roofing	9 days	Wed 1/8/25	Mon 1/20/25
38		Reconnect HVAC	5 days	Tue 1/21/25	Mon 1/27/25
39		Sheet Metal	10 days	Fri 1/24/25	Thu 2/6/25
40		**13908B**	**26 days**	**Thu 1/16/25**	**Thu 2/20/25**
41		Disconnect HVAC	3 days	Thu 1/16/25	Mon 1/20/25
42		Demolition	4 days	Tue 1/21/25	Fri 1/24/25
43		Roofing	9 days	Tue 1/21/25	Fri 1/31/25
44		Reconnect HVAC	5 days	Mon 2/3/25	Fri 2/7/25
45		Sheet Metal	10 days	Fri 2/7/25	Thu 2/20/25
46		**13908A**	**27 days**	**Wed 1/29/25**	**Thu 3/6/25**
47		Disconnect HVAC	3 days	Wed 1/29/25	Fri 1/31/25
48		Demolition	4 days	Mon 2/3/25	Thu 2/6/25
49		Roofing	9 days	Mon 2/3/25	Thu 2/13/25
50		Reconnect HVAC	5 days	Fri 2/14/25	Thu 2/20/25
51		Sheet Metal	10 days	Fri 2/21/25	Thu 3/6/25
52		**Misc Work**	14 days	Fri 3/7/25	Wed 3/26/25
53		**Demobilization**	3 days	Thu 3/27/25	Mon 3/31/25

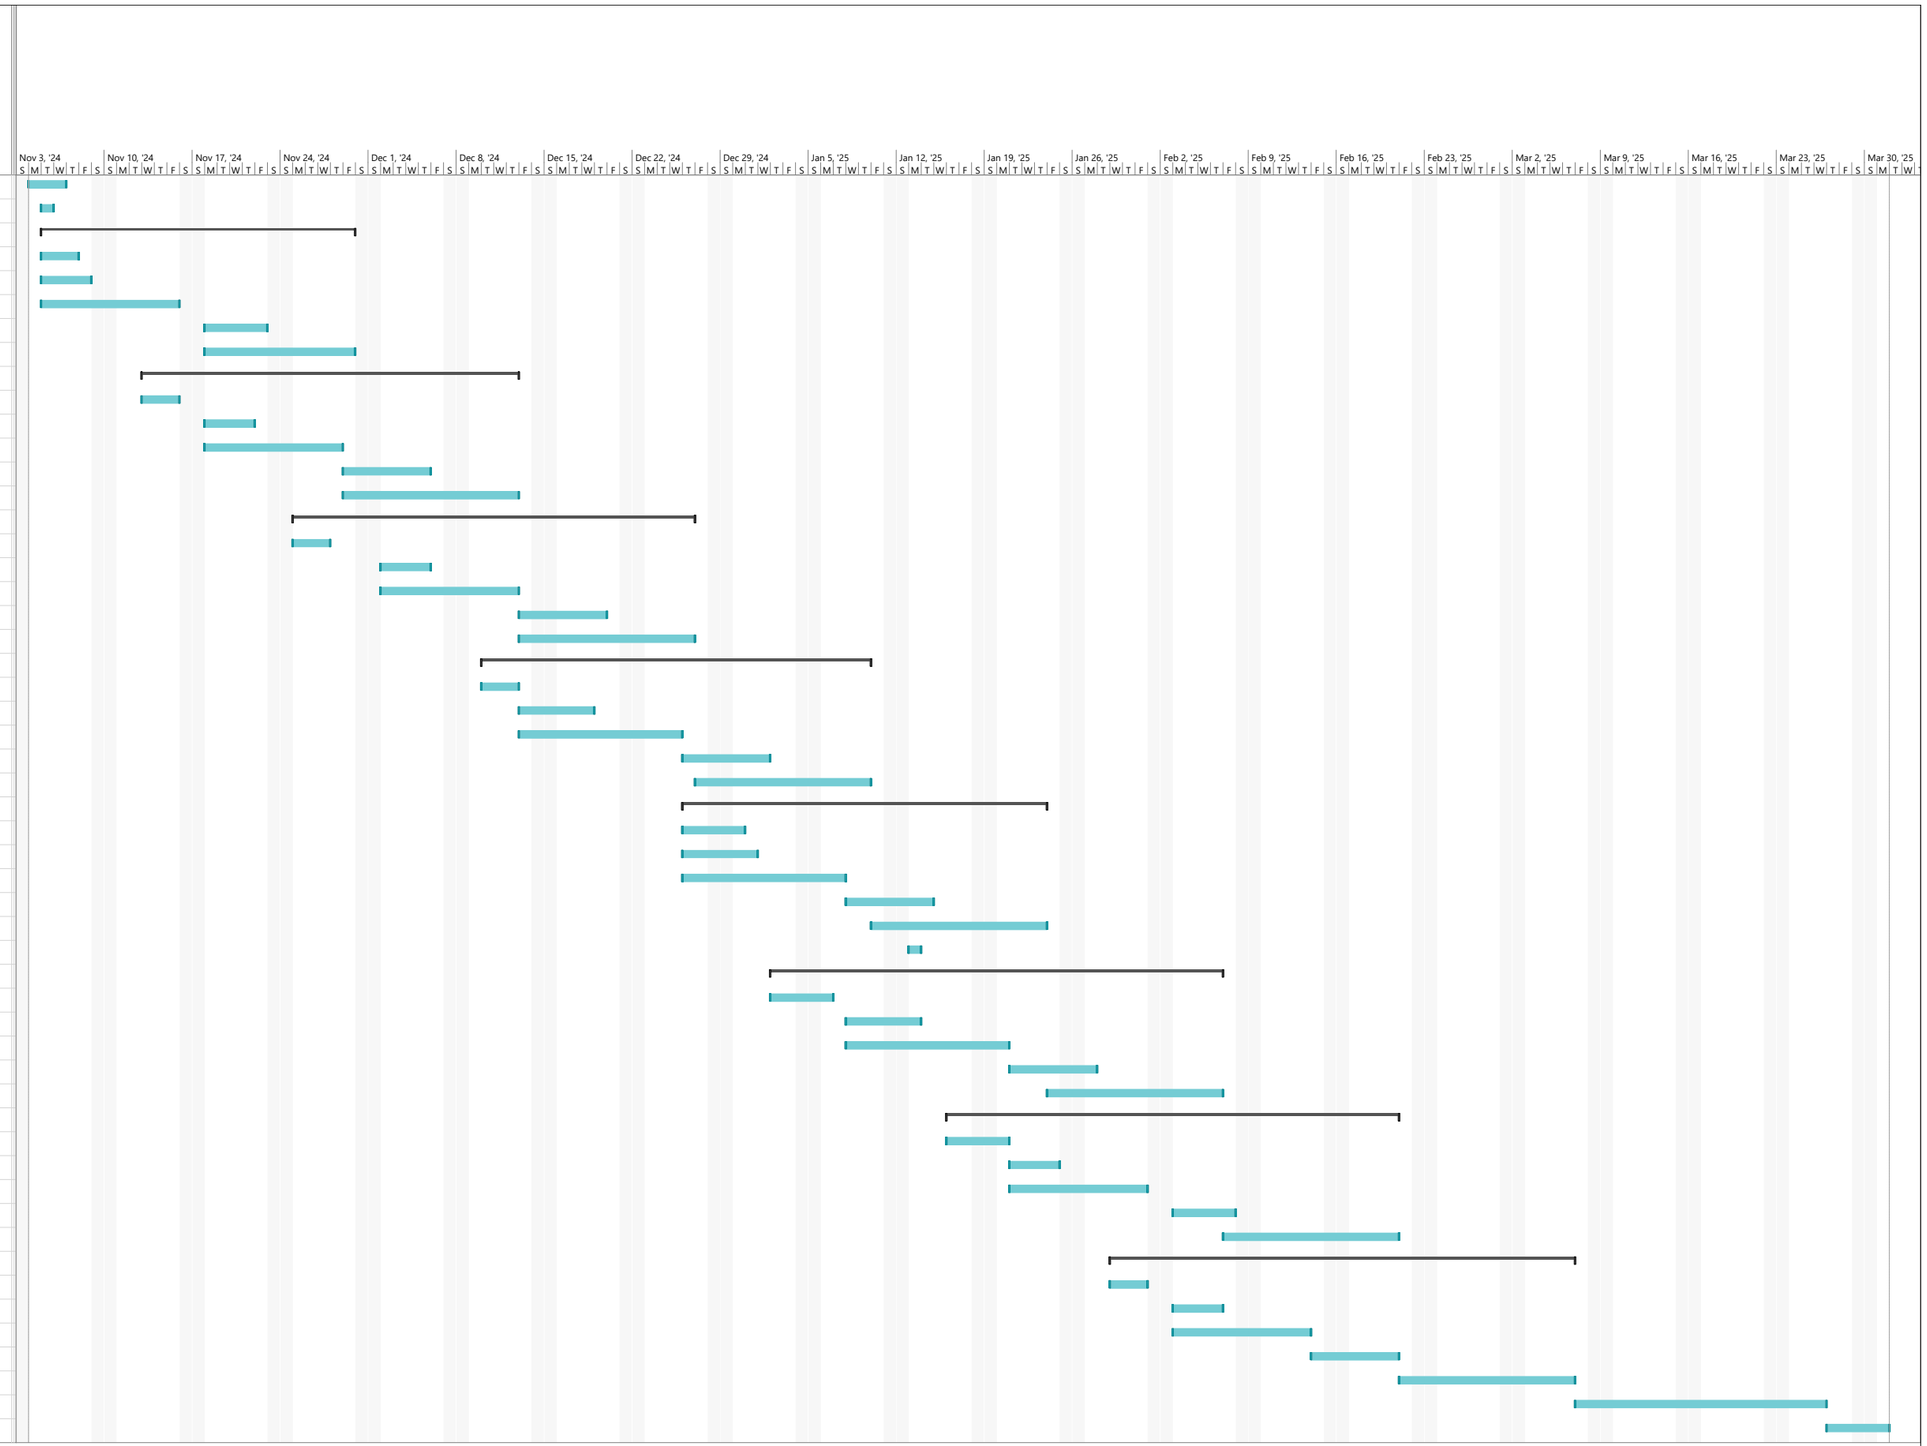

Project: Tiburon Condominium
Date: Mon 10/7/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
